

## Exam Questions PK0-005

CompTIA Project+ Certification Exam

<https://www.2passeasy.com/dumps/PK0-005/>



# NEW QUESTION 1

## DRAG DROP -

During a gate review meeting, the deliverable was rejected by the customer.

Review the dashboard.

Part 1: Drag and drop each task, placing them in the correct order based on the project change control process.

Part 2: Select the proper document(s) to be updated.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

?

2

?

3

?

4

?

5

Select the appropriate document(s) to update.

6

?

7

?

8

?

Dashboard

Question Options

Select the appropriate document(s) to update.

☐

Risk register

☐

Schedule

☐

Statement of work

☐

Organizational chart

☐

Change log

☐

Issues log

☐

WBS dictionary

A. Mastered

B. Not Mastered

Answer: A

Explanation:

Part 1

Part 2

Change Control Process

1

Define new requirements and record changes.

2

Assess the schedule, risk, and cost.

3

Update and test the deliverable.

4

Perform a demonstration.

5

Select the appropriate document(s) to update.

6

7

8

image2

Dashboard

Drag and Drop

Perform a demonstration.

Define new requirements and record changes.

Update and test the deliverable.

Consult the RACI matrix.

Assess the schedule, risk, and cost.

Obtain a sign off.

Make an announcement on the company portal.

Part 1

Part 2

Change Control Process

1

2

3

4

5

Select the appropriate document(s) to update.

6

☒ Statement of work

7

☒ Schedule

8

☒ Change log

Question Options

Select the appropriate document(s) to update.

☐ Risk register

☐ Schedule

☐ Statement of work

☐ Organizational chart

☐ Change log

☐ Issues log

☐ WBS dictionary

### NEW QUESTION 2

A project team gathers weekly to review its progress. Which of the following is the project manager MOST likely to have prepared to ensure team members who are absent remain informed about assignments?

- A. Status report
- B. Project plan
- C. Change log
- D. Meeting minutes

Answer: D

### NEW QUESTION 3

A project manager prefers to have immediate contact with team members because it allows for faster response times and more interactive discussions. Which of the following communication methods should the project manager use?

- A. Synchronous
- B. Informal
- C. Asynchronous
- D. Formal

Answer: A

### NEW QUESTION 4

As part of the planning phase, a PM has defined tasks, durations, resources, and costs. Which of the following is the NEXT step in the process?

- A. Update the work breakdown structure.
- B. Review the backlog.
- C. Seek baseline approval.
- D. Establish the resource pool.

Answer: C

### NEW QUESTION 5

A project manager realizes that a project will not be completed on time due to resource constraints. Which of the following actions should the project manager take NEXT?

- A. Trigger the contingency plan and communicate with the stakeholders.

- B. Work with the functional managers to create a work-around.
- C. Submit a change request to the change control board.
- D. Transfer the risk by hiring a new vendor who was successful on a previous project.
- E. Set up an escalation meeting with the sponsor.

**Answer:** A

#### NEW QUESTION 6

By developing a project schedule, a PM has already validated the constraints, outlined the duration of the tasks and the phases, and confirmed the proper sequence and flow of the project. Which of the following activities still needs to be performed to complete the schedule?

- A. Allocate resources.
- B. Determine the project budget.
- C. Develop a communication plan.
- D. Establish baselines.

**Answer:** D

#### NEW QUESTION 7

Which of the following should occur when implementing an IT infrastructure change that takes risks into consideration?

- A. Approving the change request
- B. Developing a rollback plan
- C. Gathering necessary resources
- D. Defining requirements

**Answer:** B

#### NEW QUESTION 8

A project manager has been very diligent in maintaining the version control for the documentation of requirements. Which of the following tools is the project manager using?

- A. Multiauthoring software
- B. Word processor
- C. Real-time polling
- D. Conferencing platforms

**Answer:** A

#### NEW QUESTION 9

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

**Answer:** B

#### NEW QUESTION 10

In a functional organization, a project has been completed successfully. Which of the following actions would the project manager MOST likely perform?

- A. Assemble a new project with existing resources.
- B. Obtain the final report from release management.
- C. Notify the functional manager that resources are released.
- D. Allocate resources in a different project.

**Answer:** B

#### NEW QUESTION 10

Which of the following activities would a project manager perform during the closing phase? (Choose three.)


- A. Lessons learned
- B. Risk analysis
- C. Removing resources
- D. Acquiring resources
- E. Statement of work sign-off
- F. Stakeholder analysis
- G. Removing access

**Answer:** AEF

#### NEW QUESTION 11

During a brainstorming session, a project team is elaborating on what caused the unexpected crash of the website that the team was developing. Given the

following:

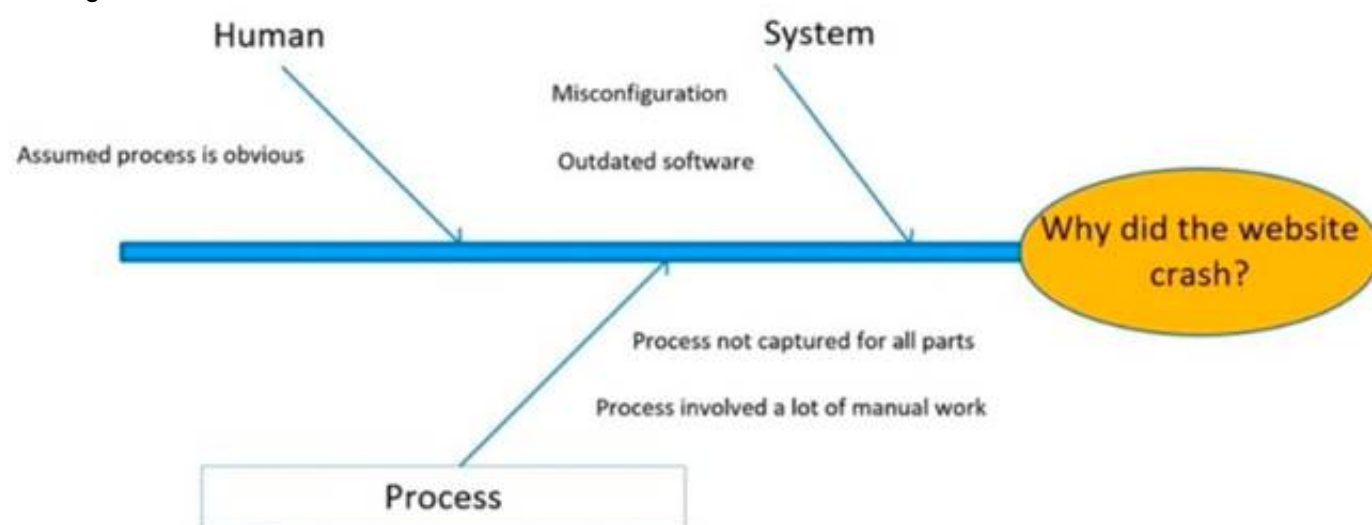

the issue?

Which of the following was the initial cause of

- A. Inadequate memory
- B. Incorrect configuration
- C. Lack of infrastructure
- D. Inadequate instructions

**Answer: B**

### NEW QUESTION 13

Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

**Answer: B**

### NEW QUESTION 18


After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

**Answer: B**

### NEW QUESTION 23

A project sponsor asked the PM to provide a summary of the current financial status. The PM uses the following burn up chart for the analysis:

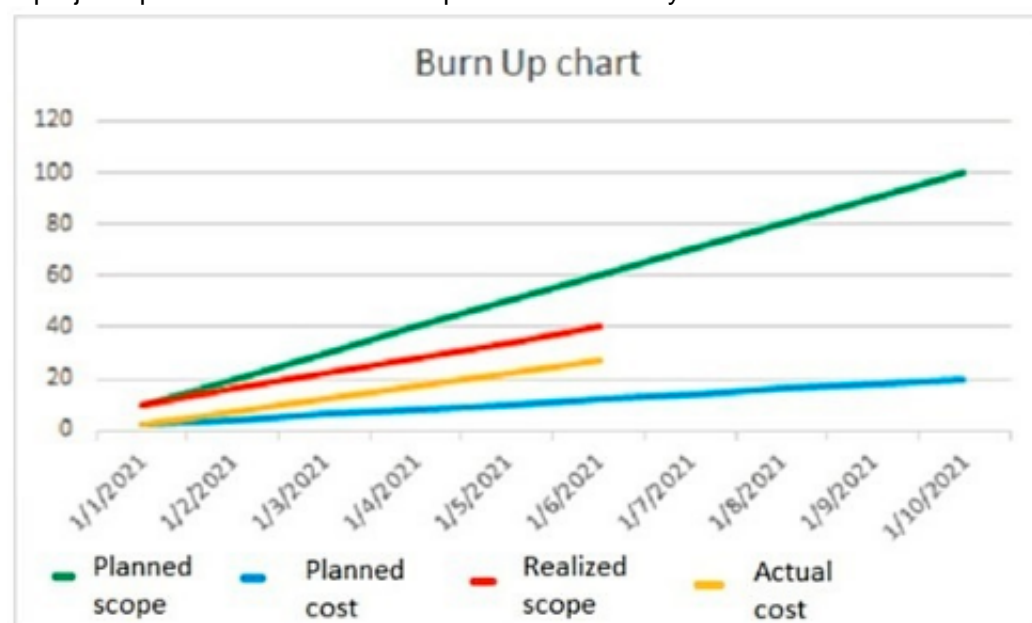

Based on the chart, which of the following is the current status of the project?

- A. Behind schedule and over budget
- B. Behind schedule and under budget
- C. Ahead of schedule and over budget
- D. Ahead of schedule and under budget

**Answer: B**

### NEW QUESTION 28

.....

## THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PK0-005 Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PK0-005 Product From:

<https://www.2passeasy.com/dumps/PK0-005/>

## Money Back Guarantee

### PK0-005 Practice Exam Features:

- \* PK0-005 Questions and Answers Updated Frequently
- \* PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- \* PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- \* PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
