

CompTIA

Exam Questions PK0-005

CompTIA Project+ Certification Exam



NEW QUESTION 1

Following a successful release, a project manager sent a survey to all stakeholders to gain an understanding of opportunity areas for the team. Which of the following can use the survey results as an input?

- A. Daily stand-up
- B. Project momentum
- C. Performance feedback
- D. Meeting minutes

Answer: B

NEW QUESTION 2

Which of the following is an activity that should be used in the closing phase of a project to support the project triple constraint?

- A. Evaluating the project
- B. Releasing the resources
- C. Closing the contracts
- D. Reconciling the budget

Answer: A

NEW QUESTION 3

During a quality analysis review, the causes of several issues have been highlighted. Which of the following should the project manager use to identify the MOST important causes?

- A. Ishikawa diagram
- B. Scatter diagram
- C. Pareto chart
- D. Decision tree

Answer: C

NEW QUESTION 4

A project manager prefers to have immediate contact with team members because it allows for faster response times and more interactive discussions. Which of the following communication methods should the project manager use?

- A. Synchronous
- B. Informal
- C. Asynchronous
- D. Formal

Answer: A

NEW QUESTION 5

As part of the planning phase, a PM has defined tasks, durations, resources, and costs. Which of the following is the NEXT step in the process?

- A. Update the work breakdown structure.
- B. Review the backlog.
- C. Seek baseline approval.
- D. Establish the resource pool.

Answer: C

NEW QUESTION 6

During the stabilization phase for recently deployed software, an end user reports a bug that is compromising data integrity. Which of the following tools will the project manager MOST likely use?

- A. Issue log
- B. Defect log
- C. Change log
- D. Task board

Answer: B

NEW QUESTION 7

A project manager has been very diligent in maintaining the version control for the documentation of requirements. Which of the following tools is the project manager using?

- A. Multiauthoring software
- B. Word processor
- C. Real-time polling
- D. Conferencing platforms

Answer: A

NEW QUESTION 8

The project team determines that software installation can only begin after the desktops have been installed and can be powered on. Which of the following dependencies does this represent?

- A. External
- B. Internal
- C. Mandatory
- D. Discretionary

Answer: B

NEW QUESTION 9


Due to budgetary and time constraints, a PM scheduled a meeting with all stakeholders during the planning phase to review the requirements and come to an agreement on the minimum viable product that would be acceptable. Which of the following would be used to document this input?

- A. Project change management plan
- B. Project management plan Most Voted
- C. Project transition plan
- D. Project communication plan

Answer: B

NEW QUESTION 10

A project team was instructed to refurbish old desktops. The following provides the details of the issues observed:

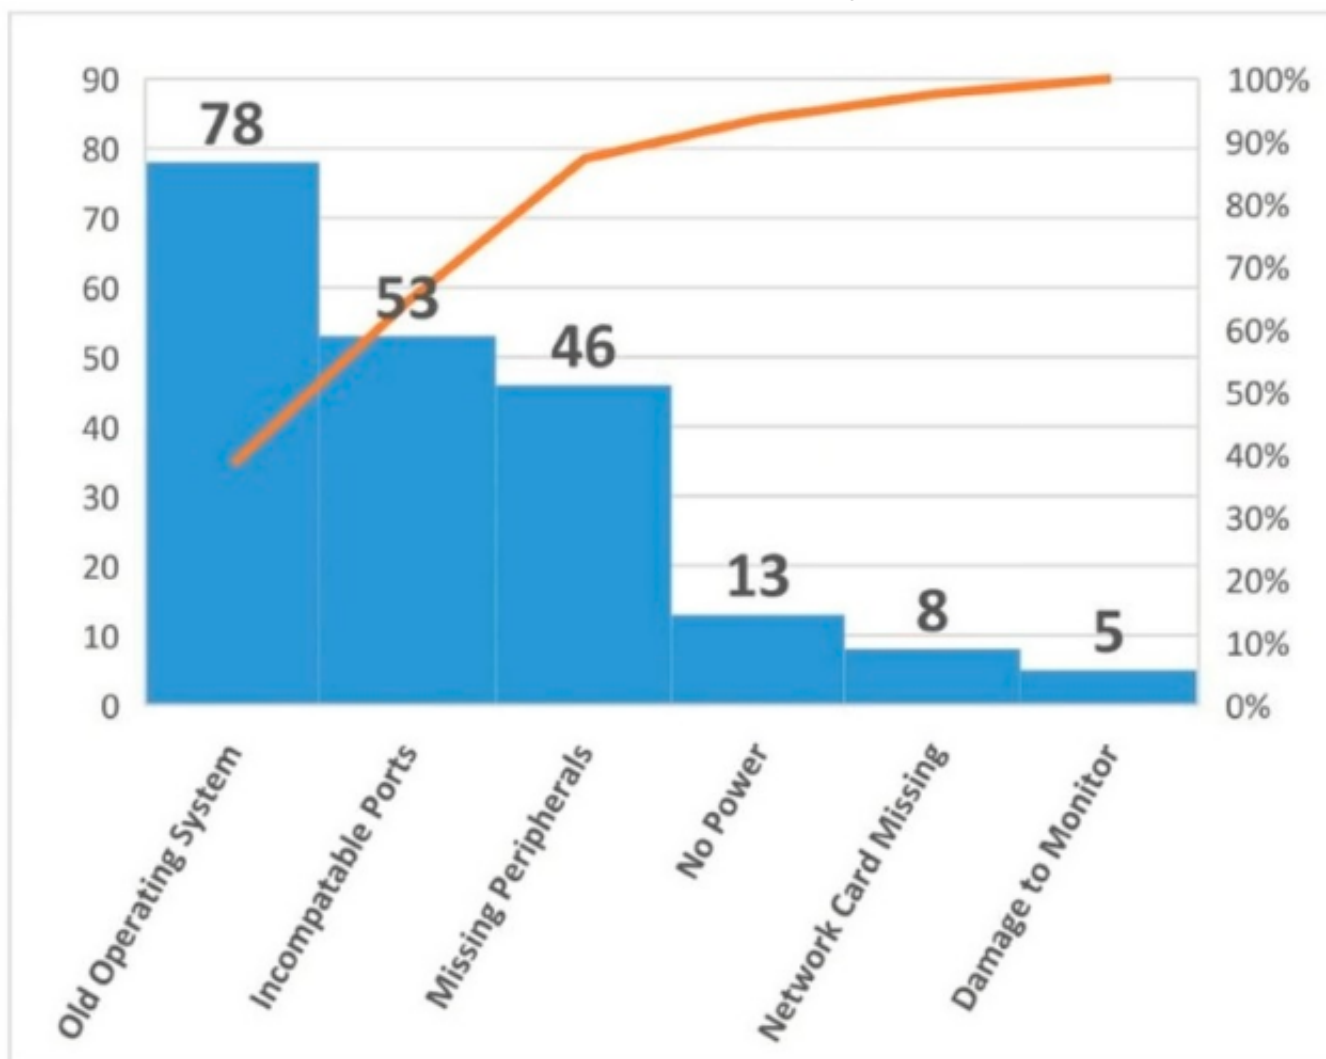

- A. Replace missing peripherals because this process can be easy and less costly.
- B. An old operating system issue has the most amount of occurrences.
- C. Damage to the monitor has the highest percentage.
- D. Address each issue as discovered to avoid rework.

Answer: A

NEW QUESTION 10

A project manager was not part of a contract negotiation. The project manager is concerned that stakeholders will expect the project to achieve deliverables requested in the RFP. Which of the following documents should the project manager produce FIRST to start communication about the boundaries of the project?

- A. Milestone chart
- B. Work breakdown structure
- C. Project charter
- D. Detailed scope statement

Answer: C

NEW QUESTION 15

A third party needs to perform a short-term task for which the duration cannot be accurately estimated and the cost cannot be calculated in advance. Which of the following should the project manager put in place before work begins?

- A. Time and materials contract
- B. Master service agreement
- C. Fixed-price contract
- D. Statement of work
- E. Cost-plus agreement

Answer: A

NEW QUESTION 20

Which of the following would be MOST beneficial to do before a call to ensure all meeting items are addressed and the correct participants attend?

- A. Assign action items to attendees.
- B. Distribute an agenda
- C. Most Voted
- D. Email the minutes from the previous meeting.
- E. Schedule a convenient time.

Answer: B

NEW QUESTION 23

While developing a project charter, a PM discovers that some of the legal requirements have not been addressed during the project concept preparation, which could result in significant financial penalties against the organization. The PM knows that implementation of appropriate changes is costly and will exceed the budget and scope of the project. Which of the following should the PM do FIRST?

- A. Escalate the finding to the change control board.
- B. Add a risk to the risk register for validation.
- C. Consult the RACI matrix to identify ownership of the risk.
- D. Have a meeting with the project sponsor and main stakeholders.

Answer: D

NEW QUESTION 26

A company that is implementing an updated version of its main product hired a new project manager to lead the project. Prior to the start of the project, the sponsor asked the project manager to prepare a report on the defects found in the previous project to avoid a decrease in production. The report shows that the two main defects are related to cosmetic and physical damage to the product. Which of the following charts would BEST prioritize which defects to address?

- A. Pareto
- B. Run
- C. Control
- D. Histogram

Answer: A

NEW QUESTION 28

A project manager has been assigned to a new project. During the planning phase, the project manager needs to get an understanding of the purpose of the project. Which of the following should the project manager do?

- A. Collate the lessons learned.
- B. Perform a gap analysis.
- C. Review existing artifacts.
- D. Conduct a retrospective.

Answer: C

NEW QUESTION 33

Due to multiple changes, the sign-off for the project scope baseline is delayed. The project sponsor has restricted the budget for this project. Which of the following should the project manager MOST likely do to move forward?

- A. Communicate with the affected stakeholders.
- B. Initiate a formal change request to modify the cost.
- C. Adjust the scope to stay within the cost.
- D. Set a new cost using a lightweight estimation method.

Answer: C


NEW QUESTION 38

As a result of an approved change, the project manager updates the project plan with the newest project end date. Which of the following change control processes should the project manager complete NEXT?

- A. Document the request in the change control log.
- B. Communicate the change deployment.
- C. Conduct an impact assessment.
- D. Implement the change.

Answer: C

Explanation:

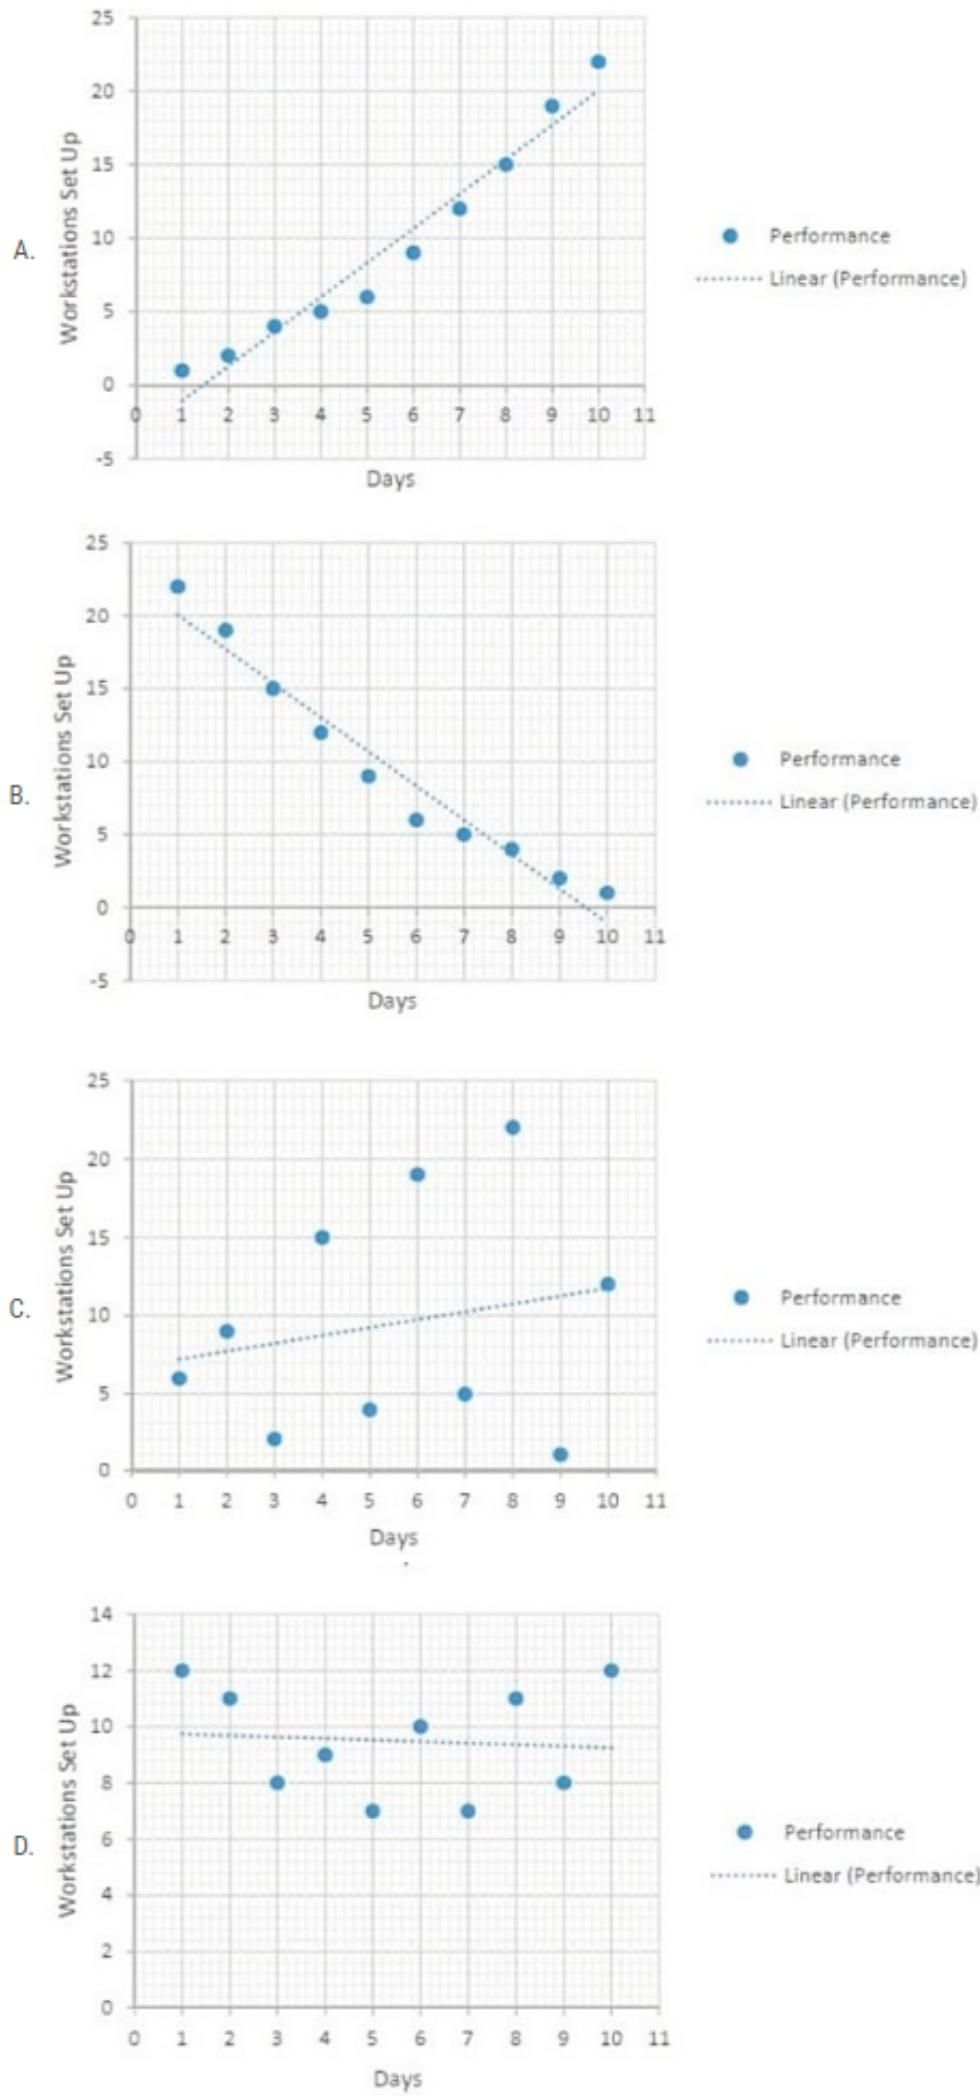

NEW QUESTION 40


An opportunity emerged in the middle of a project life cycle. Which of the following is the BEST action for the project manager to take?

- A. Exploit the risk.
- B. Accept the risk.
- C. Avoid the risk.
- D. Transfer the risk.

Answer: D

NEW QUESTION 45

During a brainstorming session, a project team is elaborating on what caused the unexpected crash of the website that the team was developing. Given the following:

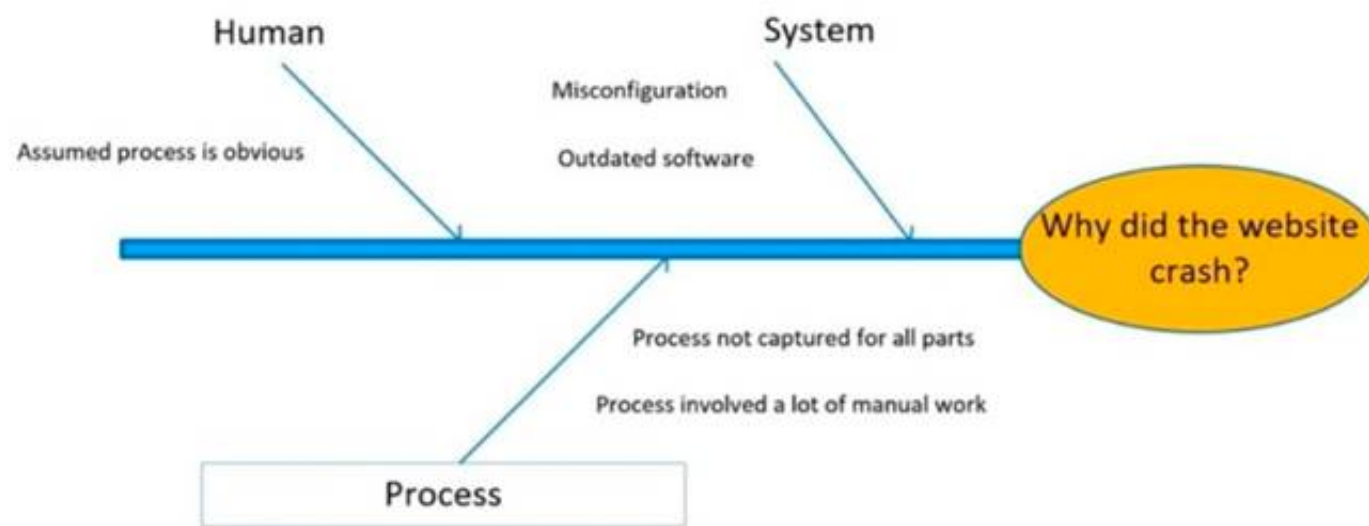

the issue?

Which of the following was the initial cause of

- A. Inadequate memory
- B. Incorrect configuration
- C. Lack of infrastructure
- D. Inadequate instructions

Answer: B

NEW QUESTION 46

Which of the following describes three-tier architecture?

- A. Conceptual, design, and implementation stages
- B. Presentation, application, and data processing
- C. Network, software, and security
- D. Development, testing, and production environment

Answer: B

NEW QUESTION 47

After determining the appropriate maintenance window, which of the following should occur NEXT in the operational infrastructure change process?

- A. Implement the change.
- B. Approve the test plan.
- C. Notify customers.
- D. Develop a rollback plan.

Answer: B

NEW QUESTION 49

A critical business initiative introduced new processes and technology to the organization. Which of the following approaches should be used to ensure the deliverables are increasingly adopted and leveraged by the organization over time?

- A. Creation of a social news forum
- B. Management directives to use the new system
- C. New user kickoff meeting
- D. Monthly feedback and training sessions

Answer: D

NEW QUESTION 51

.....

Thank You for Trying Our Product

We offer two products:

1st - We have Practice Tests Software with Actual Exam Questions

2nd - Questions and Answers in PDF Format

PK0-005 Practice Exam Features:

- * PK0-005 Questions and Answers Updated Frequently
- * PK0-005 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-005 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-005 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year

100% Actual & Verified — Instant Download, Please Click
[Order The PK0-005 Practice Test Here](#)
